


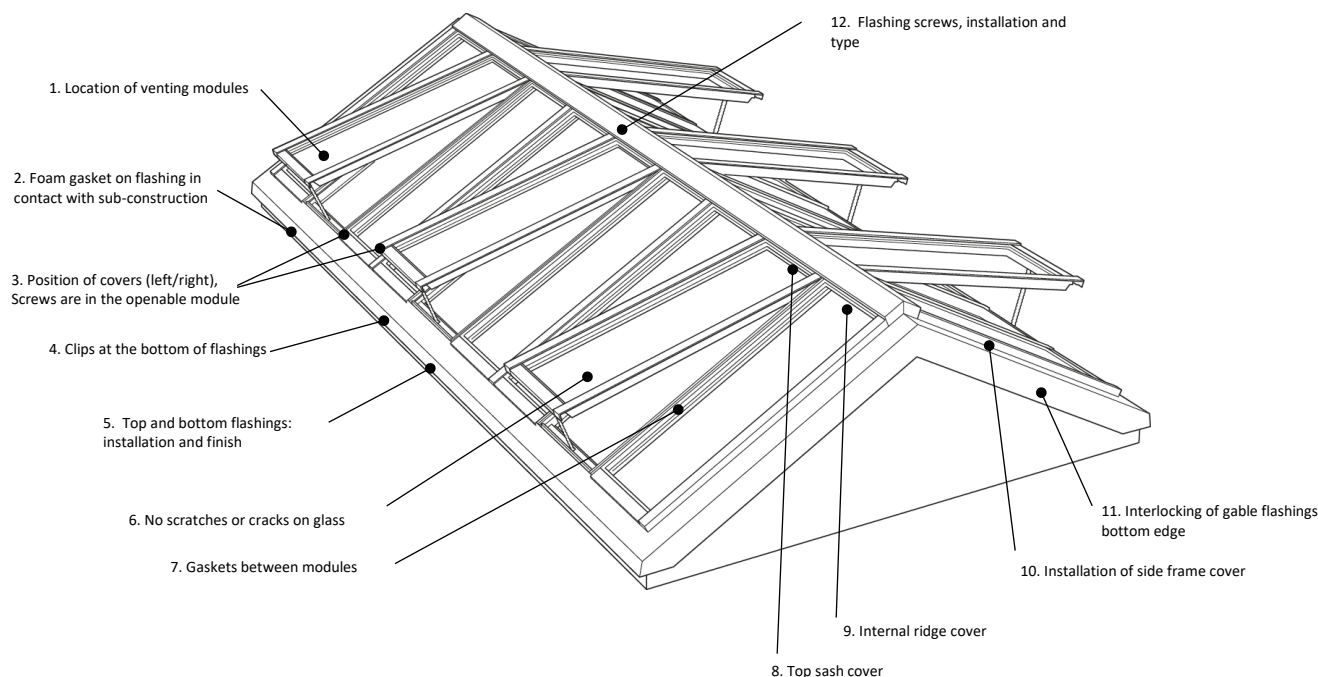

Project name:		Project no.:		Skylight no.:	
Part:					
No.:	Control points:	Control ratio:	Control method:	Remarks:	
1.	Location of venting modules	100 %	Visual		
2.	Foam gasket on flashing in contact with sub-construction	100 %	Manuel		
3.	Position of covers (left/right), Screws are in the openable module	100 %	Visual		
4.	Clips at the bottom of flashings	100 %	Visual		
5.	Top and bottom flashings: installation and finish	100 %	Visual		
6.	No scratches or cracks on glass	100 %	Visual		
7.	Gaskets between modules	100 %	Visual		
8.	Top sash cover	100 %	Visual		
9.	Internal ridge cover	100 %	Visual		
10.	Installation of side frame cover	100 %	Visual		
11.	Interlocking of gable flashings bottom edge	100 %	Visual		
12.	Flashing screws, installation and type	100 %	Visual		
13.	Electrical Components	100 %	Test		

Date:	Completed by:
-------	---------------
