


Installation End Inspection – ERC5°

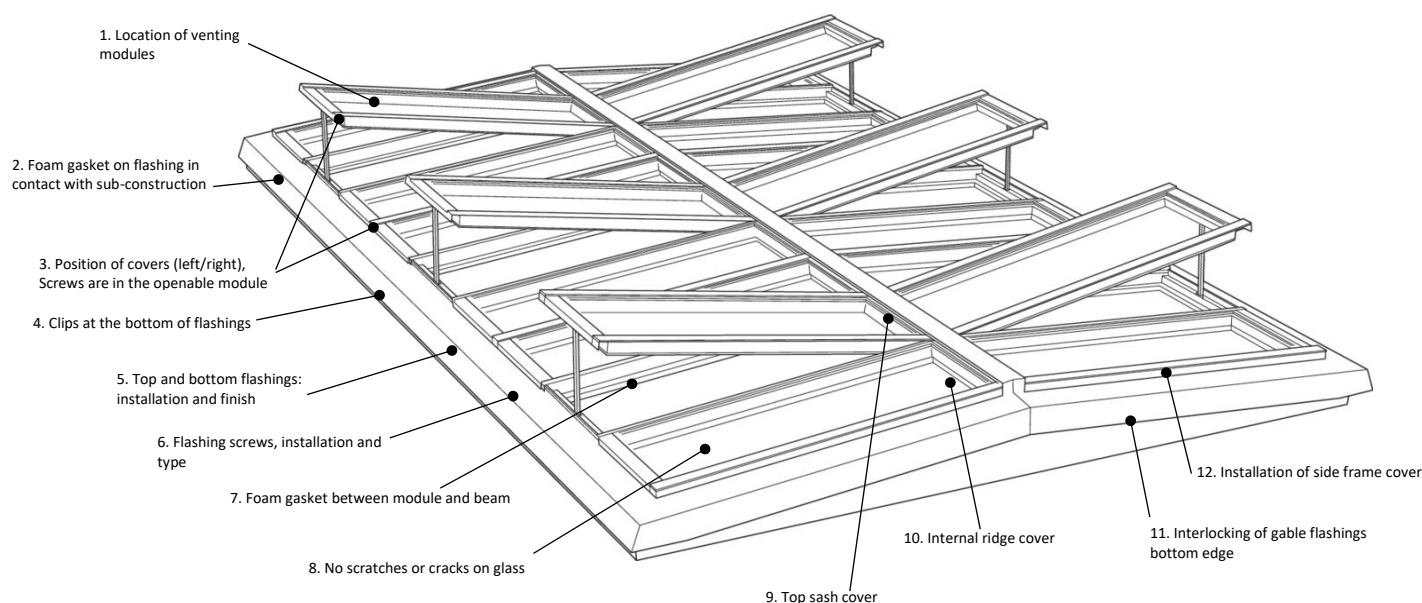

Project name:		Project no.:		Skylight no.:
Part:				
No.:	Control point:	Control ratio:	Control method:	Remarks:
1.	Location of venting modules	100 %	Visual	
2.	Foam gasket on flashing in contact with sub-construction	100 %	Manuel	
3.	Position of covers (left/right), Screws are in the openable module	100 %	Visual	
4.	Clips at the bottom of flashings	100 %	Visual	
5.	Top and bottom flashings: installation and finish	100 %	Visual	
6.	Flashing screws, installation and type	100 %	Visual	
7.	Foam gasket between module and beam	100 %	Visual	
8.	No scratches or cracks on glass	100 %	Visual	
9.	Top sash cover	100 %	Visual	
10.	Internal ridge cover	100 %	Visual	
11.	Interlocking of gable flashings bottom edge	100 %	Visual	
12.	Installation of side frame cover	100 %	Visual	
13.	Electrical Components	100 %	Test	

Date:	Completed by:
-------	---------------
